

West Side Park Project

155 S. 6th St.
Evansville, WI 53536



PROJECT TEAM

Owner:

City of Evansville

Architect/Engineer:

MSA

Aquatics Design:

Water Technology Inc.

Athletic Field Specialists:

Rettler Corporation

General Contractor:

Corporate Contractors Inc (CCI)

Construction Start:

8/30/2022

Work Completed Current Week:

- Finish install of sanitary line for bath house building
- Completed tie in that was shown completed, by the previous utility inspector off Wyler Rd. There was a 4 way installed at the location of the tie in, with a plug installed on the North side to be tied into the watermain under Wyler Road at a later date
- Completed install of water main mentioned above, with corresponding hydrant
- Continued install of fencing @ ball fields backstops
- Ideal prepped sidewalks on East half of site and installed drains under two sections of sidewalk
 - Sidewalk proof roll was completed on 4/12 with CGC on site to make recommendations.
- Pour sidewalks around playground as well as pad between soccer fields and sidewalk leading up to it
- Neuman pool continued installing rebar and prepping lap pool walls for pour next week
- Total mechanical on site to install plumbing in equipment building subgrade
- Bases for ballfield foulpoles poured

Work Completed Next Week:

- Complete tie in of water main off Windmill Ridge Rd. on Monday 4/17 and install 6" DI watermain, service for equipment building as well as hydrant
- Pour tall walls of lap pool on Tuesday 4/18 and complete pouring walls on 4/20
- Pour sump pit in pool equipment building next Tuesday
- Begin install of rebar in equipment building lower level slab
- Bath house foundations to be dug Monday 4/17 and Tuesday 4/18 of next week
- Finish install of backstop fence by 4/18 of next week
- Continue install of sidewalks on East half of the site
- Will be sending over cost to adjust grades on 10' sidewalk that ties into the existing walk off porter



City of
Evansville
www.ci.evansville.wi.gov/parkimprovements





Sidewalk around playground being poured



Soccer field pad poured with sidewalk



Sidewalk prep continues



Baseball field backstop horizontals being installed



Gates being installed @ ballfields



Water main off Wyler Dr. Tied in. North side left plugged for tie in by Fox



Sidewalk to soccer field pads prepped




Plumbing in equipment building lower level




Foul pole bases poured



Sidewalk around playground pour in progress

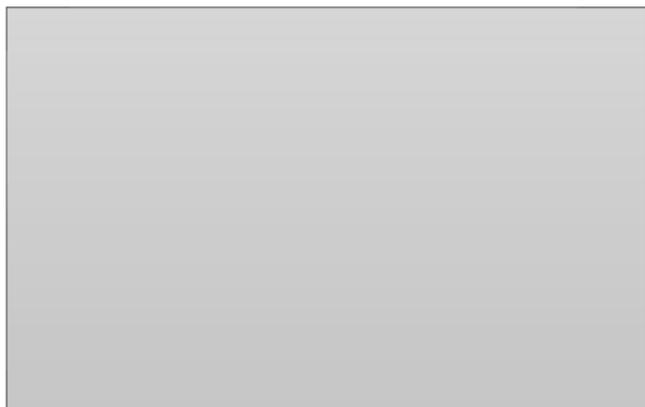

[Text]

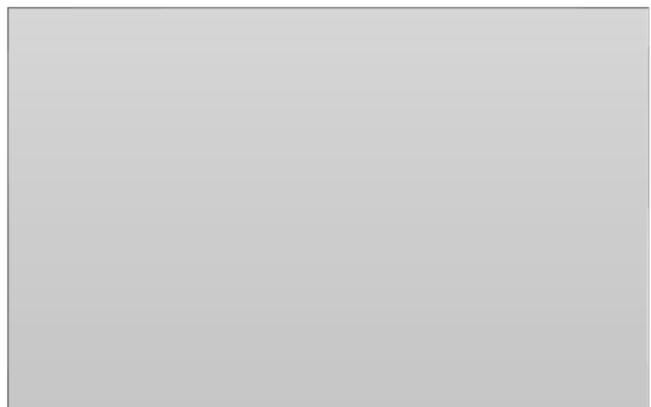

[Text]
