

West Side Park Project

155 S. 6th St.
Evansville, WI 53536



Work Completed Current Week:

- Neuman pool continued working on main drains
- Softball field seeded

PROJECT TEAM

Owner:

City of Evansville

Architect/Engineer:

MSA

Aquatics Design:

Water Technology Inc.

Athletic Field Specialists:

Rettler Corporation

General Contractor:

Corporate Contractors Inc (CCI)

Construction Start:

8/30/2022

Work Completed Next Week:

- Neuman pool to continue working on drain system/piping in pool
- Ideal Midwest to finish up baseball field topsoil and sand install as rain pushed things back to next week.
- Begin installing softball and baseball field back stops poles and fence posts
- Prep concrete area between baseball/softball fields where dugouts will sit



City of
Evansville
www.ci.evansville.wi.gov/parkimprovements






Baseball infield material stockpile and ready to spread once outfield topsoil is finished



Deep end main drain system being run and clear stone installed



Upper shallow end of pool main drains being installed

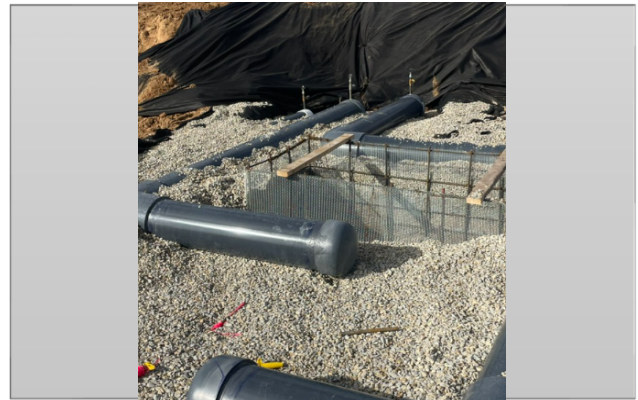

Drain basin awaiting drains to be delivered



Drain basin awaiting drains to be delivered

