

## West Side Park Project

155 S. 6th St.

Evansville, WI 53536



### Work Completed Current Week:

- Neuman pool continued to tie rebar for lap pool floor
- WTI site visit was on 3/9

### PROJECT TEAM

**Owner:**

City of Evansville

**Architect/Engineer:**

MSA

**Aquatics Design:**

Water Technology Inc.

**Athletic Field Specialists:**

Rettler Corporation

**General Contractor:**

Corporate Contractors Inc (CCI)

Construction Start:

8/30/2022

### Work Completed Next Week:

- Neuman to finish installing rebar in lap portion of pool floor
- Next scheduled pour for lap pool floor is next Wednesday 3/15
- Install wall steel after floor pour
- MSA will be on site 3/20 to survey pool and assist with pool corner layout



City of  
**Evansville**  
[www.ci.evansville.wi.gov/parkimprovements](http://www.ci.evansville.wi.gov/parkimprovements)





Rebar install @ lap portion of pool floor




Rebar install @ lap portion of pool floor




Rebar install @ lap portion of pool floor




North river section walls and floor poured and covered




X

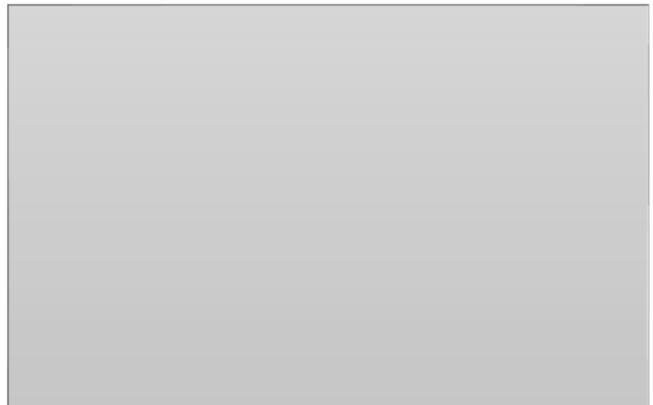


X

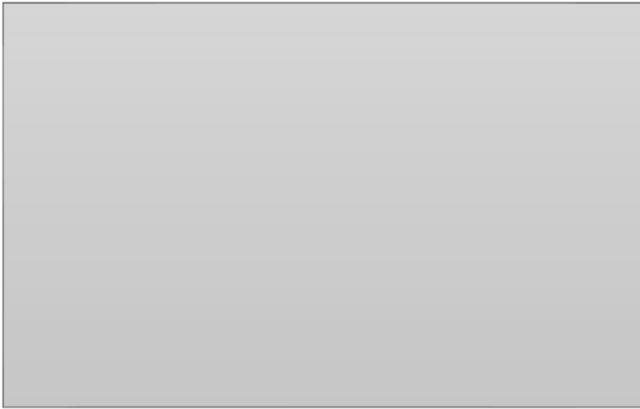


[Text]

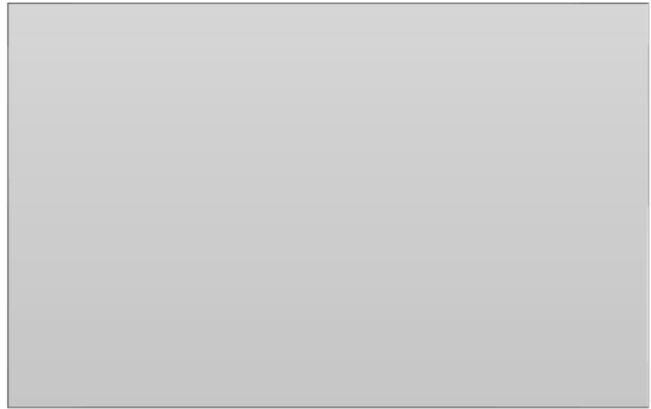


[Text]




[Text]

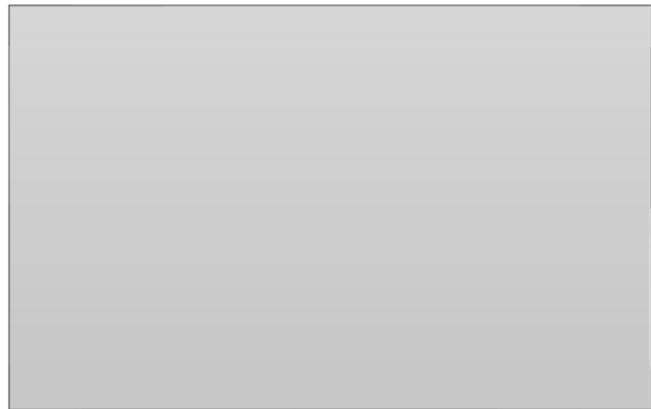

[Text]

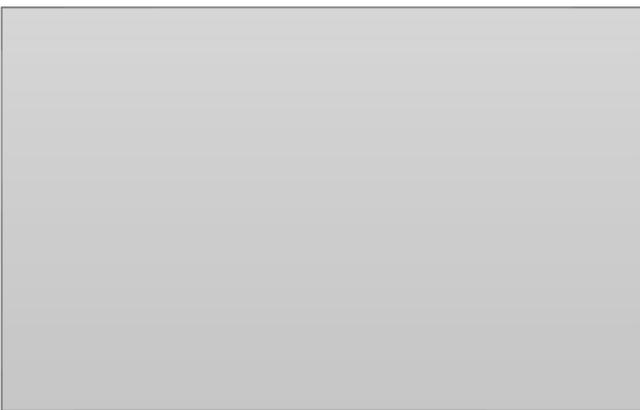

[Text]

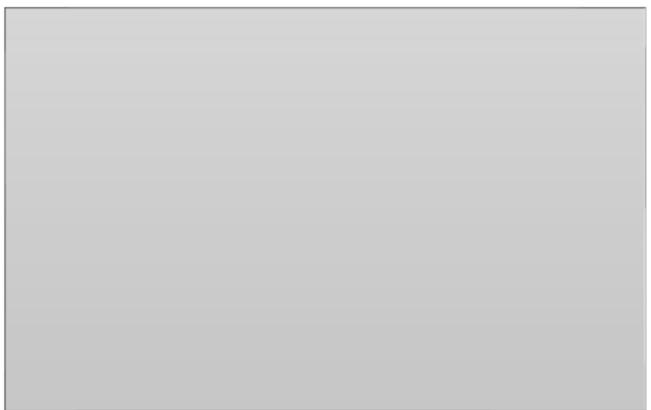

[Text]
