

West Side Park Project

155 S. 6th St.
Evansville, WI 53536



Work Completed Current Week:

- Last week and the week of 2/13, Neuman formed the floor and walls of the North section of the river portion. This was poured early last week and will send pictures when concrete balknets are removed
- Neuman pool began working on rebar in lap portion of pool floor

PROJECT TEAM

Owner:

City of Evansville

Architect/Engineer:

MSA

Aquatics Design:

Water Technology Inc.

Athletic Field Specialists:

Rettler Corporation

General Contractor:

Corporate Contractors Inc (CCI)

Construction Start:

8/30/2022

Work Completed Next Week:

- Continue working on lap portion pool floor rebar
- WTI on site for pool inspection on Friday, 3/20
- As of right now, Hughes is set to install the water lateral on the East side of the park beginning on 3/27



City of
Evansville
www.ci.evansville.wi.gov/parkimprovements





North section of river being formed



North section of river being formed




Rebar being installed for the North end of the river section



Floor rebar being installed in lap section of pool



Floor rebar being installed around pool drains in deep section

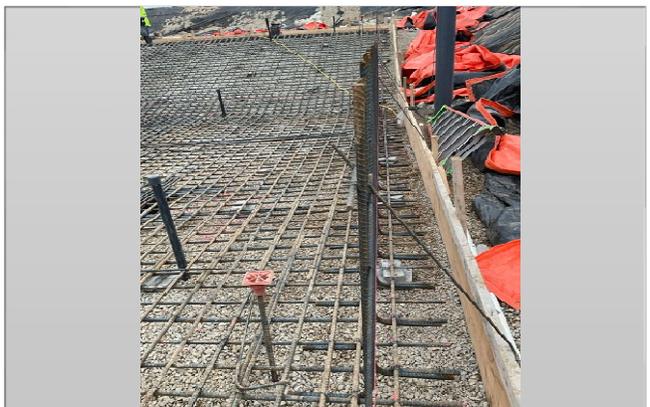

Another shot looking out of the deep end of lap portion of pool
